


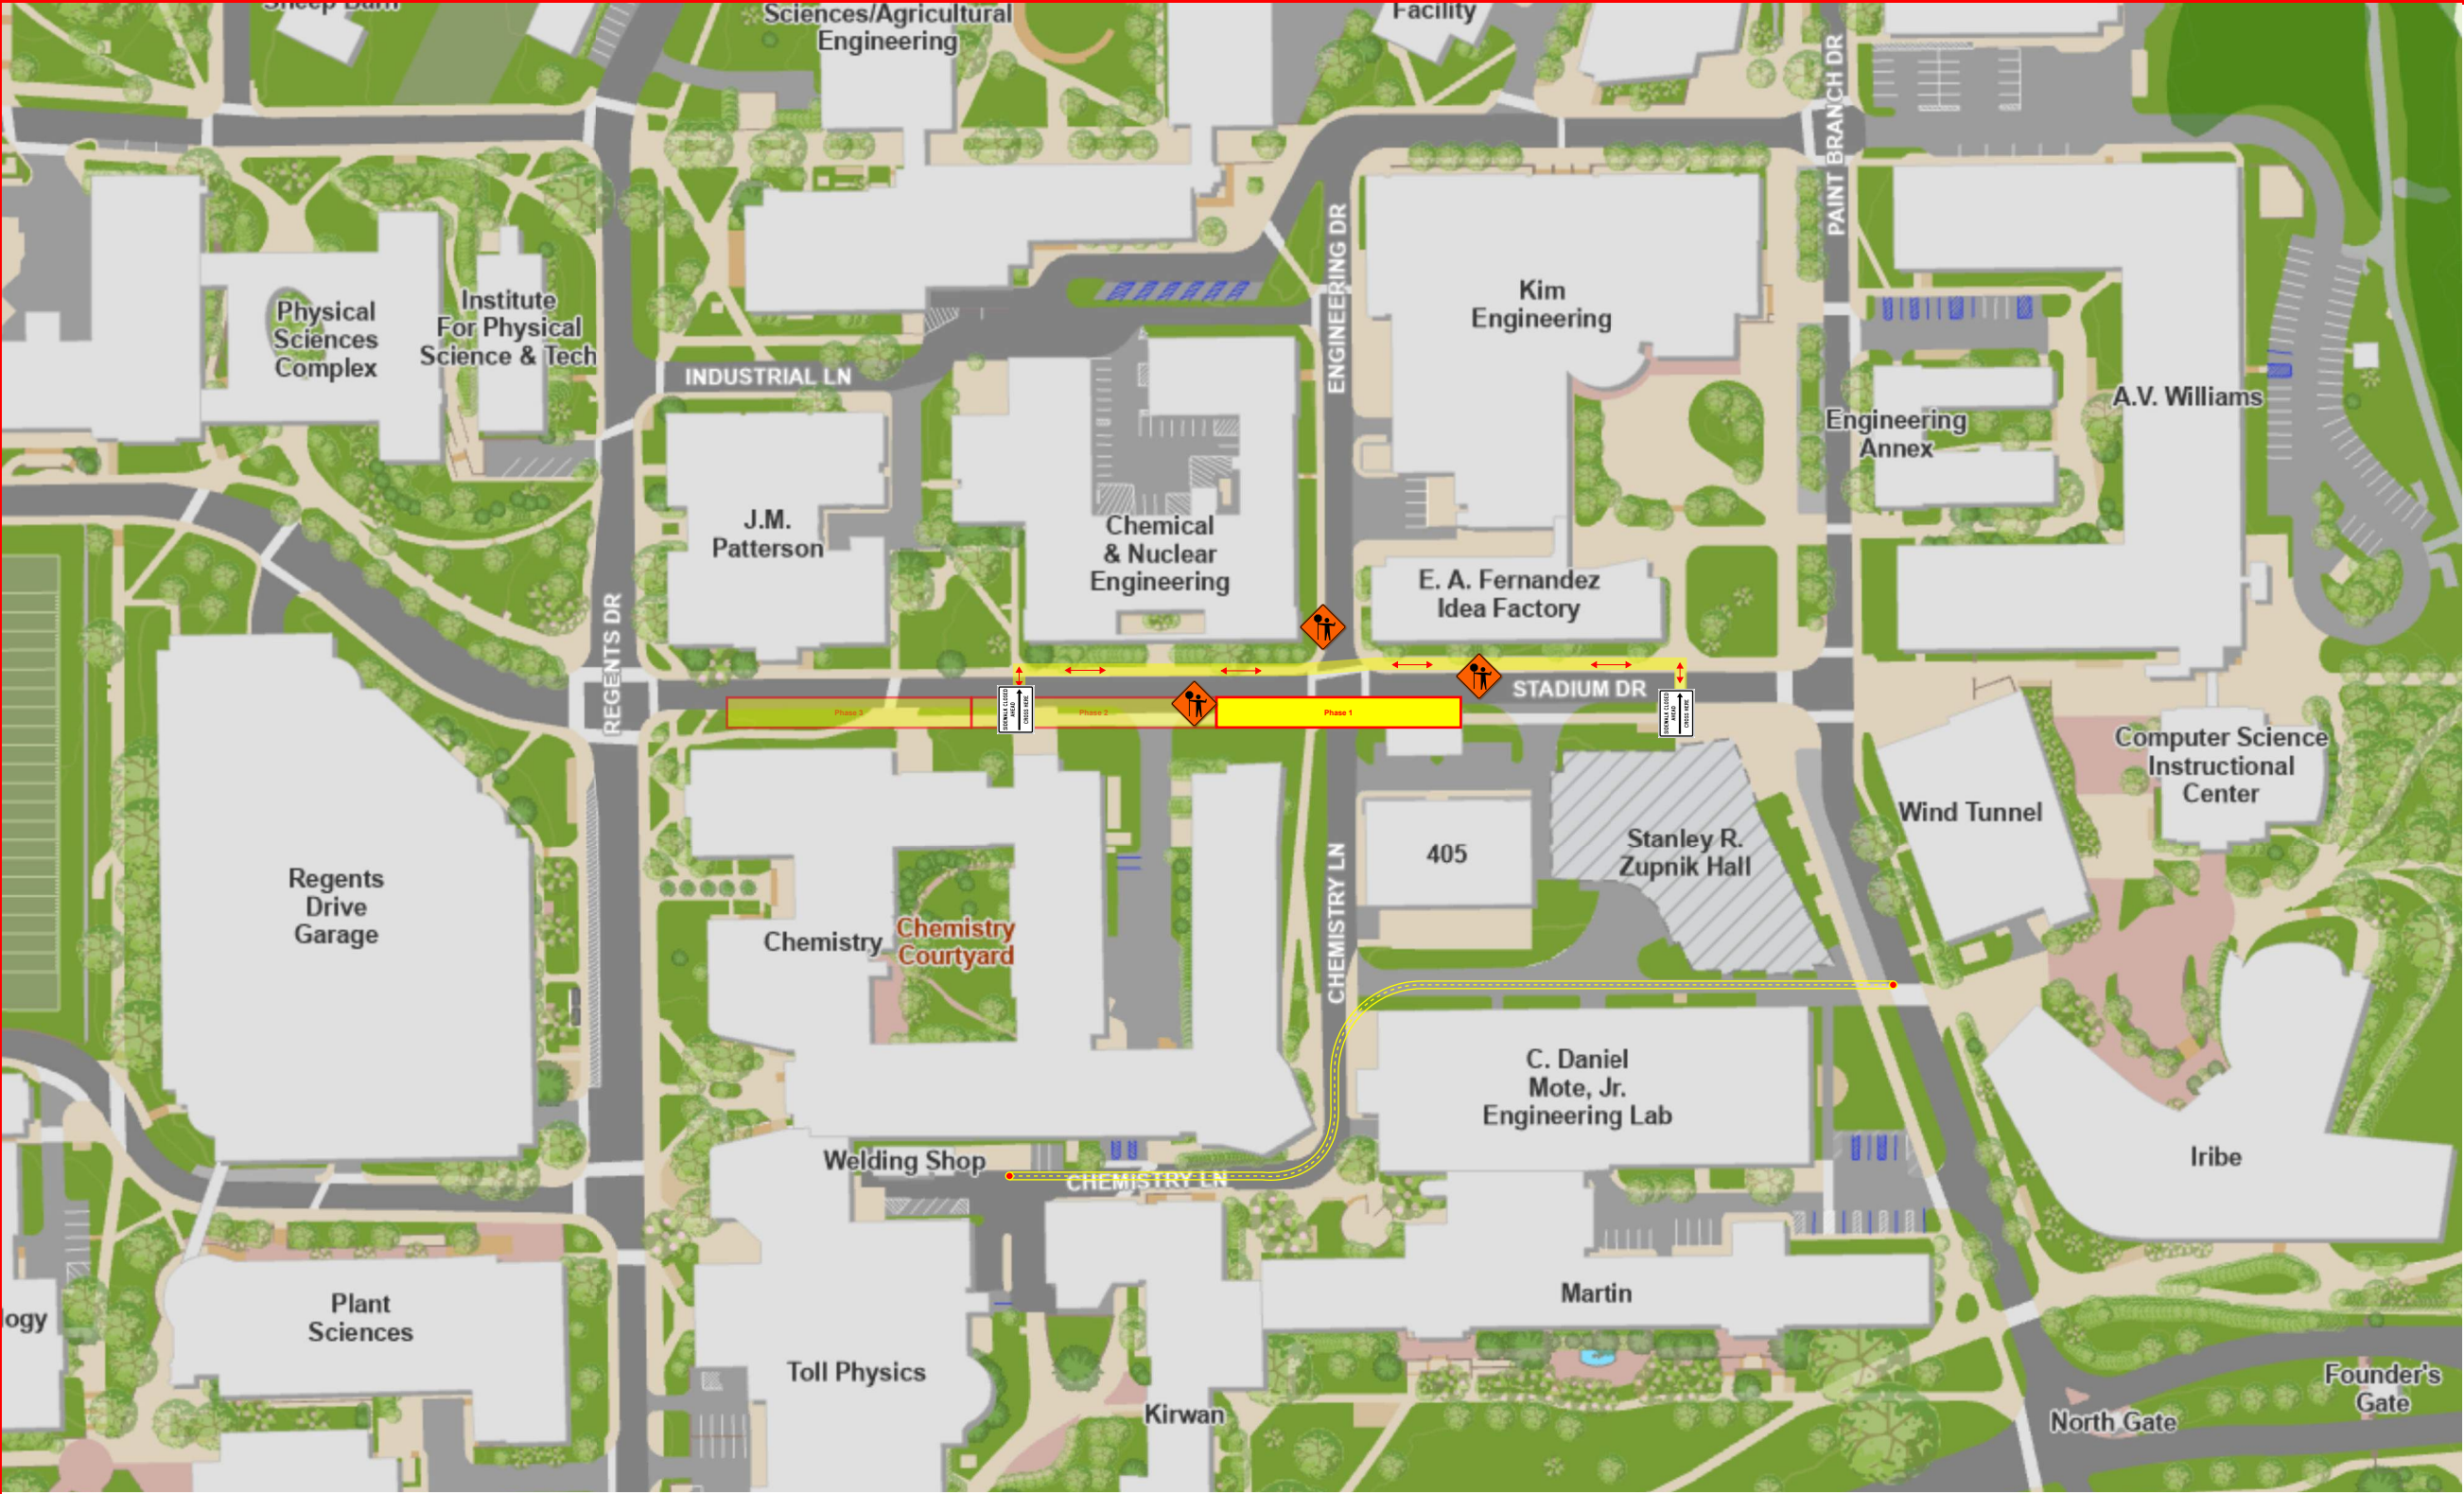

DTP-4 Renovation and Upgrade

Underground Electric Infrastructure

Phase 1 of 3

- Single Lane Closure / Work Area
- Pedestrian Detour
- EMS Detour
- Pedestrian Detour Signage
- Traffic Control Flagger Signage

Construction Activities:
Construction of an underground electrical ductbank requiring excavation within Stadium Drive. Work will be completed in three phases to minimize impacts to campus operations. Phase 1 Chemistry Lane crossing will be performed during off-hours (9:00pm-6:00am). Access to and from Chemistry Lane will be restricted to emergency personnel only during this work. A detour through Zupnik Plaza will be provided. Phase 2 and 3 to follow Phase 1 completion.

Schedule (Phase 1/3):
Target Start Date: September 8, 2026
Target Completion Date: September 15, 2026

Traffic Impacts:
A single lane of Stadium Drive will be closed during construction, with flaggers directing traffic through the work area. Chemistry Lane will be closed during off-hours while the crossing work is performed.
